










Project: PSD: Kamiak Elementary School

Date: January 31, 2019

Weather conditions:

| Date | Hi/Lo | Precip | Snow | Forecast | Avg. HI / LO |
|----------|---------|---------|--------|--|--------------|
| Thu 1/31 | 43°/34° | 0 IN | 0 IN |  Rather cloudy | 38°/27° |
| Fri 2/1 | 43°/38° | 0.13 IN | 0 IN |  Occasional afternoon rain | 39°/27° |
| Sat 2/2 | 42°/36° | 0.32 IN | 0.1 IN |  Mostly cloudy, a little rain | 39°/27° |
| Sun 2/3 | 41°/27° | 0.06 IN | 0.3 IN |  Cloudy, a rain or snow shower | 39°/27° |
| Mon 2/4 | 31°/16° | 0 IN | 0 IN |  Mostly cloudy | 39°/27° |
| Tue 2/5 | 25°/15° | 0.05 IN | 1.2 IN |  Mostly cloudy; very cold | 39°/27° |
| Wed 2/6 | 26°/17° | 0 IN | 0 IN |  Times of sun and clouds; cold | 39°/27° |

Discussion with: See Construction Progress Meeting minutes dated 1/24/19

Construction Activities:

1. Contractor to have masons return to install the precast wall cap when they clean the monument sign CMU. Currently the cap is just sitting atop the wall.






**2. Installation of Chiller
hydronic piping installation
continues.**



**3. It appears the chiller is now
on isolation pads. Chiller not
yet attached to the pad.**

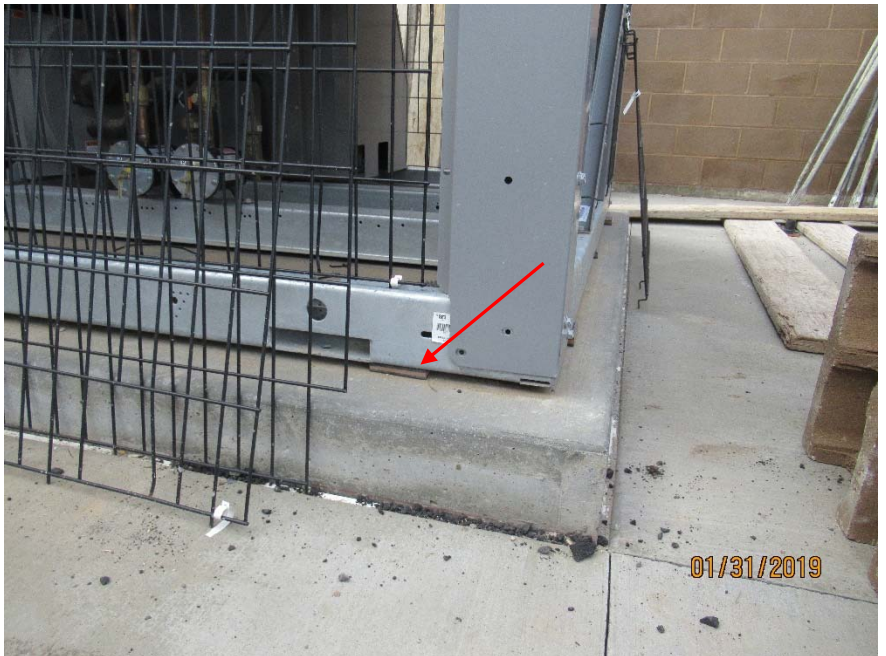



- 4. Contractor is installing sound attenuation panels in Gymnasium.**



- 5. Contractor is installing sound attenuation panels in Multi-Purpose room.**






- 6. Contractor has installed the Kitchen flooring wallbase.**



- 7. The contractor has had to trim off the bottom of the installed FRP to apply the flooring wall base. The pile of debris in this photo are the trimmed off pieces.**

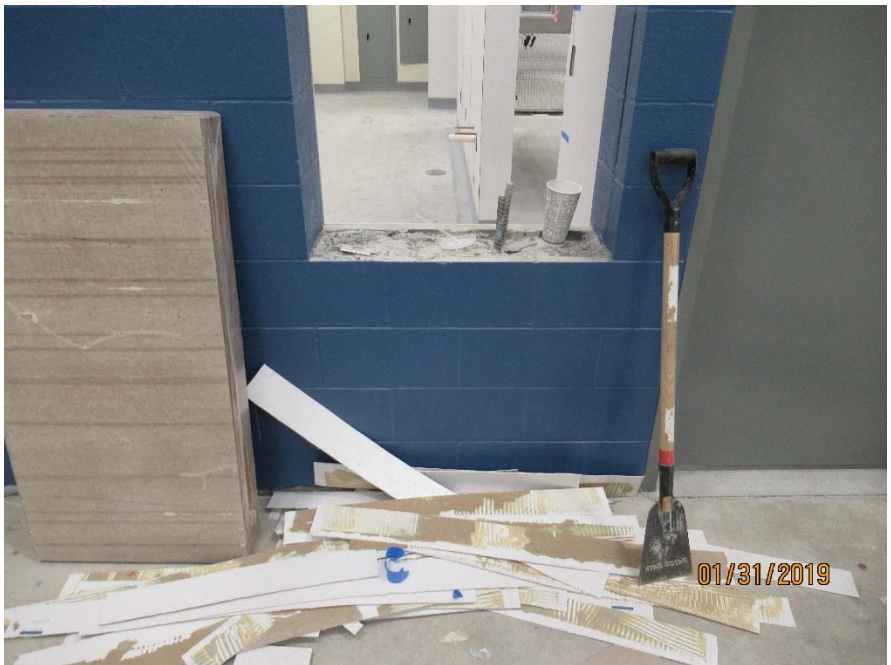



8. There appears to be an opening to the outside at the top of the wall on the southwest corner of Storage room 139A.



9. Contractor appears to have installed a sweep (not bulb type) on west exterior door 141B. The installation of bulb type sweeps were proposed by the contractor and accepted by the Architect a couple weeks ago.





- 10. It appears the contractor has begun the installation of door openers at the main entrance.**



- 11. Carpet installation is underway in Administration area.**





- 12. Contractor has installed the large window on the north wall of reception.**




- 13. There has been a change document to relocate the 2 lights and the return grill such that the lights are not over the casework.**





- 14. It appears the contractor has damaged the installed wallpaper in Health room 118C. Wall and wallpaper will need to be repaired.**

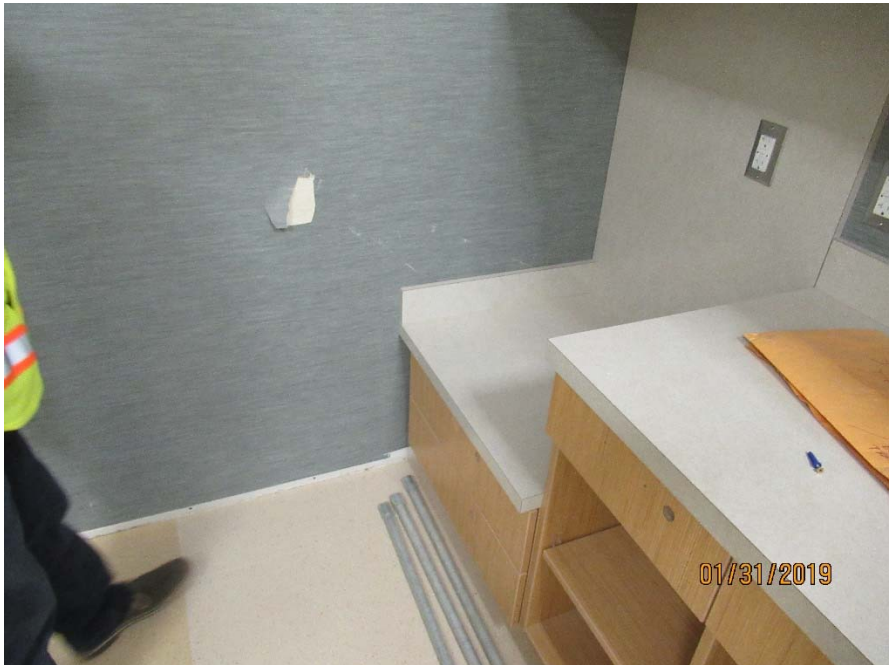


- 15. Casework per C11/A7.11 not yet installed in this opening.**





- 16. Contractor needs to repair wall in Conference room 118G where these holes were cut.**

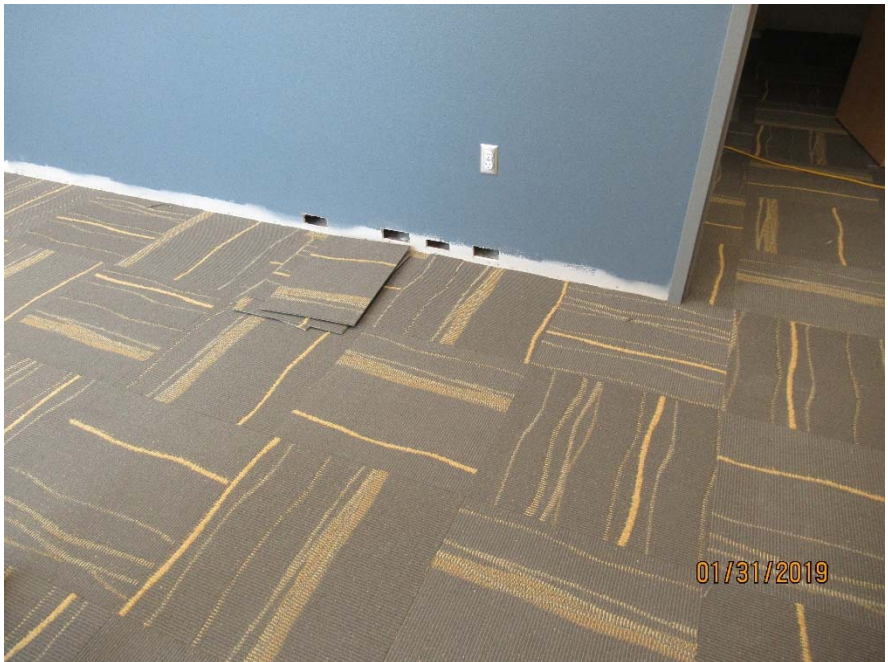


- 17. Appears the contractor has installed the tile in the Staff Workroom 118M.**





- 18. It appears the contractor has completed the installation of tile and stair nosings at south stairway.**

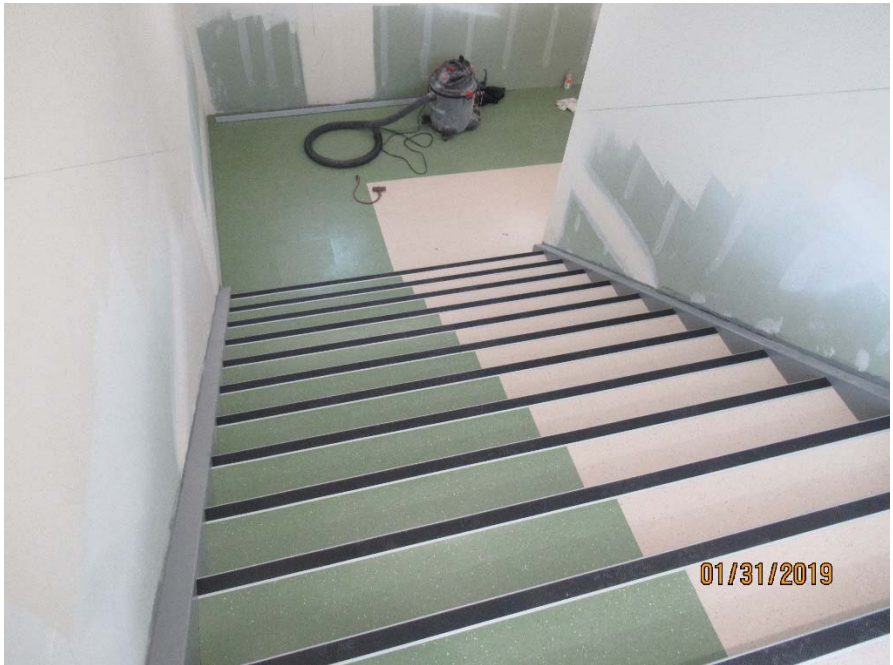

- 19. The District has turned over the TVs to the contractor for installation. Installation is in progress.**



Deficiencies: There were 4 doors noticed where the glass was broken. There are a number of other items noticed that will be documented in the Punch List phase for repair or replacement.

Dan Gordon
Project Manager

