








**Project: PSD: Kamiak Elementary School****Date: March 14, 2019****Weather conditions:**

Date	Hi/Lo	Precip	Snow	Forecast	Avg. HI / LO
Thu 3/14	38°/25°	0 IN	0 IN	 Partly sunny	49°/32°
Fri 3/15	42°/28°	0 IN	0 IN	 Clouds and sun; fog, chilly	49°/32°
Sat 3/16	45°/29°	0 IN	0 IN	 Fog in the morning; some sun	49°/32°
Sun 3/17	45°/28°	0 IN	0 IN	 Intervals of clouds and sun	50°/32°
Mon 3/18	50°/31°	0 IN	0 IN	 Mostly sunny	50°/32°
Tue 3/19	55°/34°	0 IN	0 IN	 Plenty of sun	50°/32°
Wed 3/20	59°/36°	0 IN	0 IN	 More sunshine than clouds	50°/33°

**Discussion with:** See Construction Progress Meeting minutes dated 3/14/19**Construction Activities:**

1. It appears the motorized roller shades at the high translucent panels in the Multi-Purpose room have been installed.





2. Contractor appears to have installed the curtain track. Contractor stated the curtain is scheduled to be installed on April 1<sup>st</sup>.



3. Carpet on stage steps has been installed.





- 4. The Freezer and Cooler appear to have been started up. The information panels are powered and appear to be in alarm.**



- 5. The floor covering installation in the north stair is nearly complete.**





- 6. Appears the contractor has taken delivery of the accepted Bid Alternate #4 movable shelving. Contractor was directed to place 3 shelving units in each classroom and the rest in the Library.**



- 7. Appears the contractor has taken delivery of the accepted Bid Alternate #4 movable shelving. Contractor was directed to place 3 shelving units in each classroom and the rest in the Library.**





- 8. Contractor has begun installation of the window sills.**



- 9. Built in bench on the upper floor has been installed.**






- 10. Contractor has caulked the cement board floor joints in the Mezzanine. There is still an application of painted on surfacing that needs to be applied.**



- 11. FRP paneling in the main entry has been installed as has the control panels.**

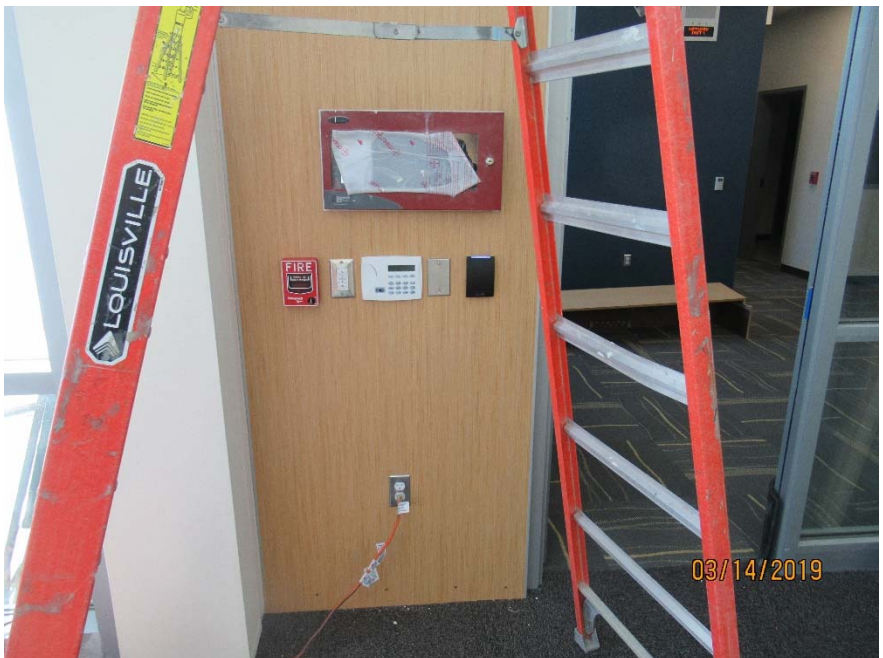



- 12. Testing And Balancing is underway in the Library and the final few areas where not yet completed. The building Air Barrier Testing is scheduled for tomorrow 3/15/19.**



- 13. Owner and Architect approved this mock-up for the elevator shaft walls. The vertical reveals to go through the horizontal reveals.**



**Deficiencies: None noticed at this time. Any challenges in this report can easily be a part of the Punch List if the Contractor hasn't addressed the issue beforehand.**

**Dan Gordon**  
Project Manager

