








**Project: PSD: Kamiak Elementary School****Date: March 21, 2019****Weather conditions:**

Date	Hi/Low	Precip	Snow	Forecast	Avg. HI / LO
Thu 3/21	57°/34°	0 IN	0 IN	 Mostly sunny	51°/33°
Fri 3/22	54°/39°	0.03 IN	0 IN	 Sunny to partly cloudy	51°/33°
Sat 3/23	49°/35°	0.06 IN	0 IN	 A bit of morning rain	51°/33°
Sun 3/24	47°/36°	0 IN	0 IN	 Mostly cloudy	51°/33°
Mon 3/25	57°/35°	0.06 IN	0 IN	 Some sun, then turning cloudy	52°/33°
Tue 3/26	50°/33°	0.01 IN	0 IN	 Overcast	52°/34°
Wed 3/27	51°/34°	0.06 IN	0 IN	 Mostly cloudy	52°/34°

**Discussion with:** See Construction Progress Meeting minutes dated 3/21/19**Construction Activities:**

1. Appears snow is melting rather quickly. Contractor should be able to place this missing piece of sidewalk in the next couple weeks.





2. Once the snow is melted and the ground is not too wet the fencing contractor should be back to mend fencing and finish installation of fencing.




3. Contractor has repaired the wall tile at the drinking fountains across the hall from the Multi-Purpose room.







4. Contractor working on drilling holes for the attachment of the north stair nosings.

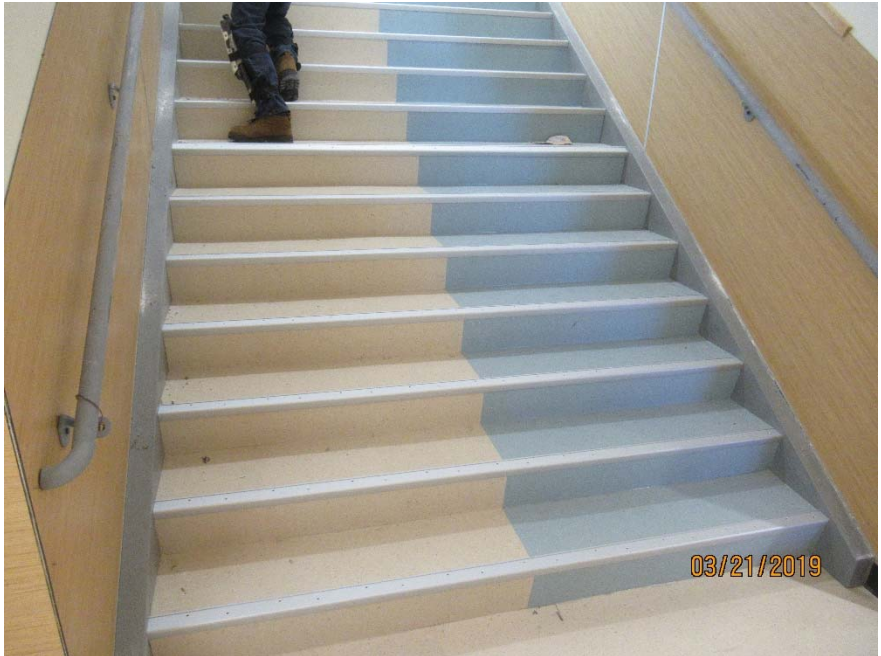

5. It appears the contractor is making quick work of installation of the chair rail in the corridors.





- 6. Contractor working on drilling holes for the attachment of the main (center) stair nosings.**



- 7. Floor tile appears complete with the exception of area adjacent the elevator doors and the landing between.**







8. Contractor has not yet installed the casework in Office 118J. I can only assume it will be delivered with the island casework for the Staff Workroom.



9. Corridor FRP appears installed for the most part. The temp heaters have been removed.





- 10. Contractor has the cleaning crew working on the second floor.**



- 11. The contractor has repaired the floor/west wall juncture in Storage room 139A and sealed the concrete floor.**





12. It appears the door swing in the Kitchen bathroom has not yet been changed. I mentioned to the contractor and he said he would chase it down.



13. It appears more parts for the playground have been delivered.



**Deficiencies:** None noticed at this time. Any challenges in this report can easily be a part of the Punch List if the Contractor hasn't addressed the issue beforehand.

**Dan Gordon**  
Project Manager

