








**Project: PSD: Kamiak Elementary School****Date: May 23, 2019****Weather conditions:**

	Date	Hi/Lo	Precip	Snow	Forecast	Avg. HI / LO
THU	5/23	74°/49°	0 in	0 in	 Times of clouds and sun	67°/44°
FRI	5/24	63°/43°	0.16 in	0 in	 A t-storm in the area; cooler	67°/44°
SAT	5/25	66°/45°	0.07 in	0 in	 Mostly cloudy	67°/44°
SUN	5/26	72°/47°	0.08 in	0 in	 Clouds and sun, a few showers	67°/44°
MON	5/27	74°/50°	0.15 in	0 in	 Some sun, a couple of showers	68°/44°
TUE	5/28	75°/51°	0 in	0 in	 Mostly cloudy	68°/44°
WED	5/29	73°/51°	0 in	0 in	 A couple of showers possible	68°/45°

**Discussion with:** See Construction Progress Meeting minutes dated 5/23/19.**Construction Activities:**

1. Landscaping contractor continues installing sprinkler system. Walker meeting with Curtis Concrete concerning concrete edging not yet installed.





2. Landscaping contractor continues installing trees. Walker meeting with Curtis Concrete concerning concrete edging not yet installed.



3. Walker needs to schedule the ADA parking area striping as well as signage install.





4. I mentioned to the contractor this appears to be metal wall framing exposed to the elements. If not addressed before hand this will show up on the building exterior Punch List. Possible location of air passage.

No indication that the frame has been sealed against the split faced CMU.



5. Although it appears the contractor has core drilled some of the required holes in the concrete for the install of exterior guard rails at the Library and the Stage exterior doors, they are not finished and not yet installed.






6. I mentioned to the contractor this appears to be metal wall framing exposed to the elements. If not addressed before hand this will show up on the building exterior Punch List. There are a number more locations with this condition. Possible a location of air passage (See below).



7. This is a photo of the exterior side of Storage room 243, where there is air passing through the area. There appears to be no visual indicator that the contractor has sealed between the CMU and window frame.

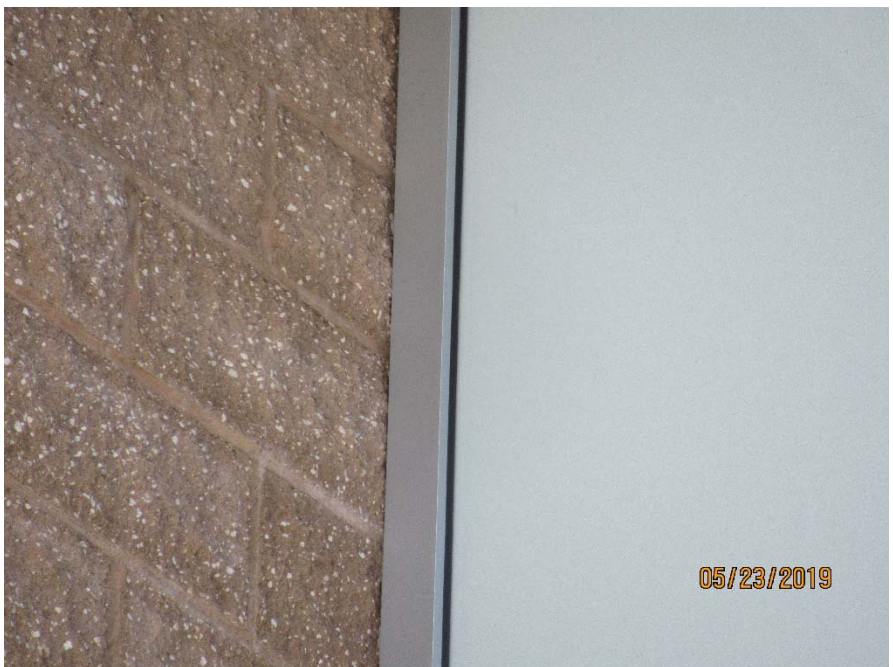



- 8. It appears no progress has been made on ADA ramp. Walker meeting with Curtis Concrete.**

**Fencing contractor expected to be back on site next week Tuesday to continue fence install as well as repair.**



- 9. Fencing contractor expected to be back on site next week Tuesday to continue fence install as well as repair.**





**10. Avista has returned to level installed utility boxes.**



**11. Avista has returned to level installed utility boxes.**





- 12. Contractor has installed the new door frame for the Kitchen bathroom.**



- 13. Painter is painting main entry steel and soffit.**



**Deficiencies: None noticed at this time. Contractor needs to finish up inside the building and finish site work.**

**Dan Gordon**  
Project Manager

