








**Project: PSD: Kamiak Elementary School****Date: June 21, 2018****Weather conditions:**

Date	Hi/Low	Precip	Snow	Forecast	Avg. HI / LO
Thu 6/21	76°/56°	0.11 IN	0 IN	 A brief morning shower or two	73°/47°
Fri 6/22	77°/53°	0 IN	0 IN	 Partly sunny; pleasant	73°/47°
Sat 6/23	72°/52°	0 IN	0 IN	 Times of clouds and sun; nice	74°/47°
Sun 6/24	81°/58°	0 IN	0 IN	 Plenty of sunshine	74°/47°
Mon 6/25	78°/49°	0 IN	0 IN	 Clouds and sunshine; nice	74°/47°
Tue 6/26	71°/48°	0 IN	0 IN	 Times of sun and clouds	75°/48°
Wed 6/27	74°/50°	0 IN	0 IN	 Partly sunny	75°/48°

Discussion with: See Construction Progress Meeting dated 6/21/18.**Construction Activities:**

1. It appears the developer's contractor has installed 2 manholes.






- 2. Earthwork contractor continues to move material from borrow site, pictured here to the playfield west of Kamiak.**



- 3. Insulation contractor injecting insulation in CMU cores.**

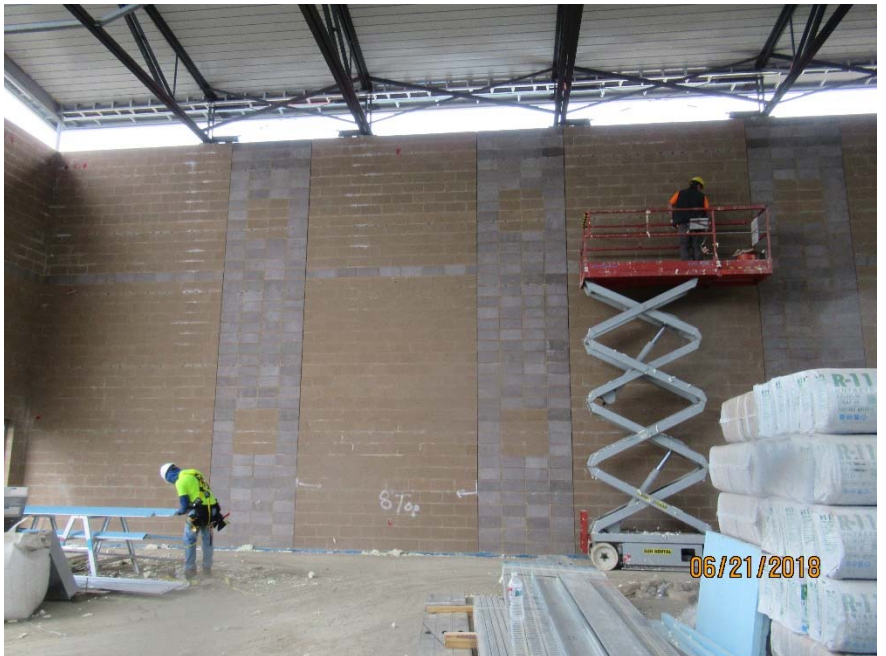




- 4. Appears there is water coming up through floor cleanouts on the lower floor. When asked the contractor states this is from testing the sewer line.**



- 5. Appears there is water coming up through floor cleanouts on the lower floor. When asked the contractor states this is from testing the sewer line.**

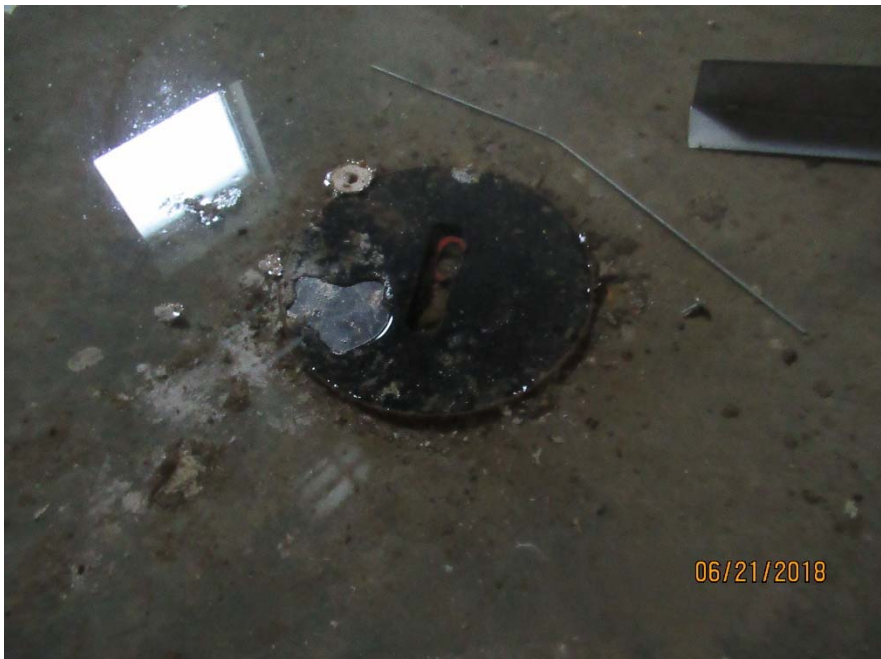



- 6. Roofing contractor appears to be installing flashing on lower roof.**



- 7. Appears the contractor has installed the fascia on the east roof edge of Area A.**





8. Appears the contractor has staged wallboard and will be installing in the next week.



9. Ductwork and wallboard staged in classrooms in Area A upper floor.





10. Ductwork and wallboard staged in classrooms in Area A upper floor.



11. There are a number of roof leaks where the wind driven rain gets under the ice and water shield.



Deficiencies: No issues noticed at this time.

Dan Gordon
Project Manager

