








**Project: PSD: Kamiak Elementary School****Date: June 6, 2019****Weather conditions:**

Date	Hi/Lo	Precip	Snow	Forecast	Avg. HI / LO
THU 6/6	54°/40°	0.12 in	0 in	 Clouds breaking for some sun	69°/46°
FRI 6/7	58°/41°	0.01 in	0 in	 Mostly cloudy; breezy	69°/46°
SAT 6/8	61°/41°	0 in	0 in	 Mostly cloudy; cool	70°/46°
SUN 6/9	70°/46°	0 in	0 in	 Pleasant and warmer	70°/46°
MON 6/10	77°/51°	0 in	0 in	 Clouds and sun; delightful	70°/46°
TUE 6/11	82°/55°	0 in	0 in	 Partly sunny; very warm	70°/46°
WED 6/12	87°/58°	0 in	0 in	 Sun and clouds	70°/46°

**Discussion with:** See Construction Progress Meeting minutes dated 6/6/19.**Construction Activities:**

1. Landscaper continues to install plantings, irrigation and bark.





2. **Landscaper continues to install plantings, irrigation and bark.**



3. **Fence contractor is installing the north property line vinyl fence.**








- 4. Fence contractor setting fence posts in concrete.**



- 5. It appears the last rain event has caused some erosion onto asphalt play area and access road. Landscaper will put soil back in place before hydroseeding.**

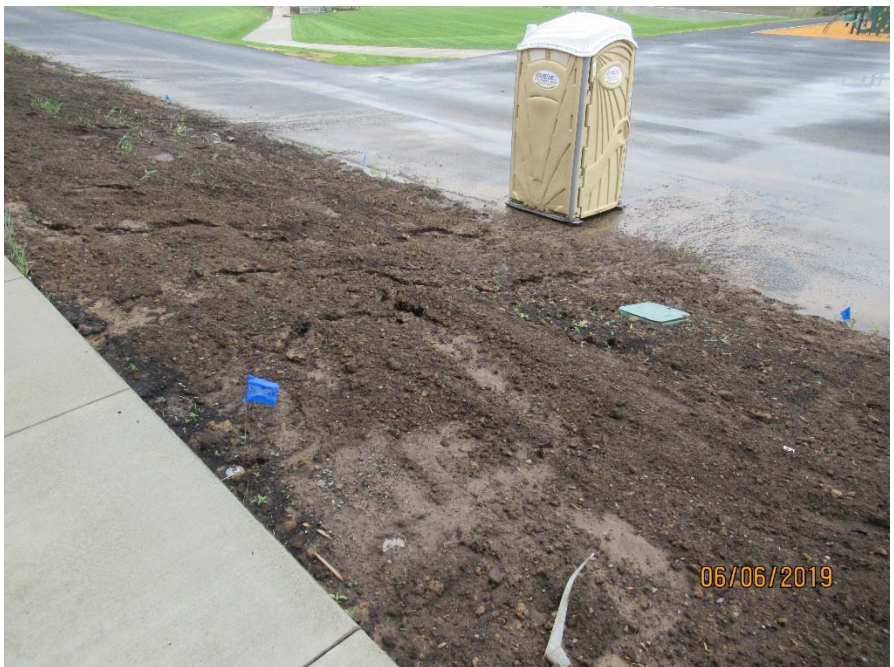



- 6. Fence contractor has placed fence frame for this enclosure fence piece.**



- 7. Fence contractor has placed fence frame and begun stringing fence for this enclosure fence piece.**







- 8. Landscaper has accepted delivery of sod for the remaining areas that are to receive sod.**



- 9. Landscaper installing sod at lower play field.**

**It appears the fence contractor has framed the top of the back stop. The fabric has not yet been installed.**





- 10. The contractor that placed the sloped (south) portion of the ADA access walk damaged the asphalt path. They have removed that portion of the asphalt. Upon review I noticed not enough of the asphalt has been removed. I informed the contractor.**



- 11. As mentioned above the sloped (south) portion of ADA access sidewalk has been placed.**







- 12. Contractor has set the bike racks, still need to place the concrete.**



- 13. Contractor has begun installation of the FRP paneling at the elevator shaft.**





- 14. Contractor has installed the island work station along with the electrical outlets in Staff Workroom 118M.**



- 15. Contractor has sealed around the chiller piping in Storage room 139A.**



**Deficiencies: None noticed at this time. Contractor needs to finish up inside the building and finish site work.**

**Dan Gordon**  
Project Manager

