



## Observation Report

Dan Gordon, Senior Project Manager  
P: 509.323.2748 - F: 509.323.2758

**Project: PSD: Kamiak Elementary School**

**Date: January 25, 2018**

### Weather conditions:

Date	Hi/Lo	Precip	Snow		Forecast	Avg. HI / LO
Thu 1/25	40°/31°	0.05 IN	0.3 IN		A p.m. rain or snow shower	38°/27°
Fri 1/26	37°/31°	0.08 IN	0.6 IN		Periods of sun, snow showers	38°/27°
Sat 1/27	40°/38°	0.51 IN	2 IN		Snow at times, 1-3"	38°/27°
Sun 1/28	45°/42°	0.27 IN	0 IN		Periods of rain	38°/27°
Mon 1/29	48°/38°	0.15 IN	0 IN		Remaining cloudy and mild	38°/27°
Tue 1/30	43°/30°	0.27 IN	0.8 IN		Breezy with a little snow	38°/27°
Wed 1/31	42°/28°	0 IN	0 IN		Snow or flurries possible	38°/27°

**Discussion with:** See Construction Progress Meeting Minutes Dated 1/25/18.

### Construction Activities:

1. Appears contractor is digging down the dirt hill north of the site to get to dry soil to use as backfill.





**2. Appears the contractor has formed the slab for the chiller.**



**3. Masons continue laying up the Gymnasium walls.**







**4. Contractor has set three of the Kitchen trusses.**



**5. Looking south: Appears the contractor is in the process of installing the trusses from grid line A to M.**





**6. Metal deck is installed and being tacked in place from grid line A to M.**



**7. Contractor is placing underslab electrical conduits on ground floor.**








**8. Appears the contractor has begun installing exterior metal studs.**



**9. Standing on metal deck on the upper floor, looking north.**

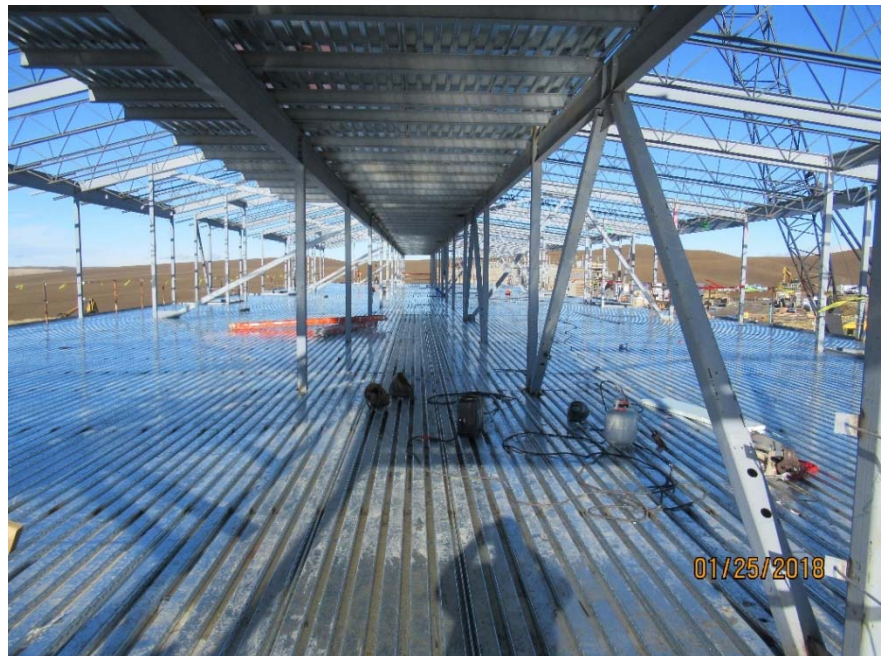



**10. Standing on metal deck on the mezzanine, looking north.**



**11. Contractor has accepted delivery of Fan Coil Units that will be installed on the mezzanine.**







**12. Contractor has accepted delivery of Fan Coil Units that will be installed on the mezzanine. The Units in the distance are those shown in photo 11 above.**



**Deficiencies:** None noticed at this time.

**Dan Gordon**  
**Senior Project Manager**

