








**Project: PSD: Kamiak Elementary School****Date: January 3, 2019****Weather conditions:**

Date	Hi/Low	Precip	Snow	Forecast	Avg. HI / LO
Thu 1/3	37°/34°	0.06 IN	0.1 IN	 Rain and snow showers	35°/24°
Fri 1/4	42°/33°	0 IN	0 IN	 Mostly cloudy	35°/24°
Sat 1/5	42°/34°	0.03 IN	0 IN	 Cloudy	36°/24°
Sun 1/6	39°/29°	0.11 IN	0.1 IN	 A bit of snow and rain	36°/25°
Mon 1/7	37°/32°	0.12 IN	0.4 IN	 Cloudy, a rain or snow shower	36°/25°
Tue 1/8	44°/39°	0.14 IN	0 IN	 Cloudy, spotty showers	36°/25°
Wed 1/9	45°/35°	0.13 IN	0.2 IN	 Considerable cloudiness	36°/25°

Discussion with: See Construction Progress Meeting minutes dated 1/3/19**Construction Activities:**

1. The gymnasium floor has been installed, sanded, sealed and the contractor is taping off for the striping. Striping colors were approved today.





2. It appears the contractor is preparing to install piping to the chiller.



3. I reminded the contractor to be sure and attach the chiller to the slab.





4. It appears the water off the roof is flowing to the double doors 135B that go into Janitors room 135. We have had water intrusion through this door before the threshold was installed.



5. This is the inside of door 135B. The contractor has installed the threshold and caulked it to keep the water out.





6. Contractor is installing FRP panels in the Kitchen.



7. Appears the plumbers still needs to install the fixtures in the Kitchen restroom 143A.





8. It appears the contractor has drilled 2 holes at either side and 4 holes in the back of the projector box in the Multi-Purpose room. I question if this is enough to allow cross ventilation for the projector. I informed the team at the progress meeting that I felt the side walls and the back wall should be removed to open the projector box to the soffit area allowing maximum cross ventilation.



9. Contractor continues installation of casework in Library as well as other locations in the building as spaces become ready.





10. Casework shelving in the Library.



11. Contractor has installed some of the break metal dividers where the wall meets the window frame.





- 12. The contractor has installed
One (1) break metal corner
piece at Classroom 106.**



- 13. Contractor continues to
install VCT in the upper
floor main hallway.**






- 14. It appears the contractor has begun installing sinks and fixtures in upper level classrooms.**



- 15. Elevator shaft appears ready to receive the elevator. Contractor has informed the team delivery is expected the second or third week of March.**

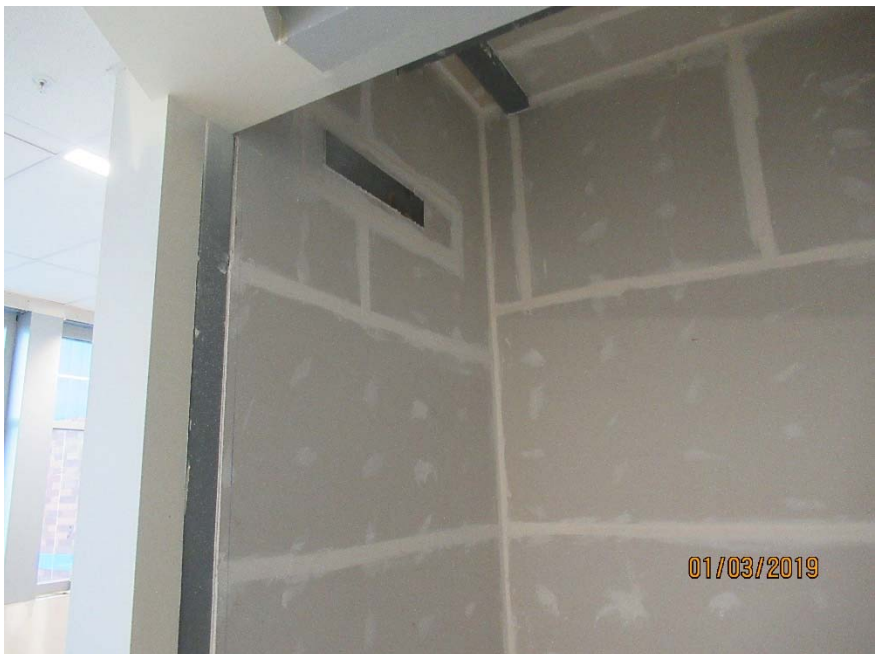

Deficiencies: No deficiencies noticed at this time.

Dan Gordon
Project Manager

