








**Project: PSD: Kamiak Elementary School****Date: October 18, 2018****Weather conditions:**

Date	Hi/Low	Precip	Snow	Forecast	Avg. HI / LO
Thu 10/18	64°/39°	0 IN	0 IN	 Brilliant sunshine; pleasant	59°/36°
Fri 10/19	68°/43°	0 IN	0 IN	 Plenty of sun; mild	59°/36°
Sat 10/20	70°/43°	0 IN	0 IN	 Plenty of sun; mild	58°/35°
Sun 10/21	70°/40°	0 IN	0 IN	 Plenty of sun; mild	58°/35°
Mon 10/22	67°/41°	0 IN	0 IN	 Partly sunny; mild	57°/35°
Tue 10/23	66°/42°	0.06 IN	0 IN	 Increasing cloudiness; mild	56°/35°
Wed 10/24	58°/42°	0.07 IN	0 IN	 A couple of showers possible	56°/35°

Discussion with: See Construction Progress Meeting dated 10/18/18.**Construction Activities:**

1. Temp road still in place.





2. Contractor is placing north parking lot light pole bases.



3. More north parking lot light pole bases, also contractor is placing sidewalk along the north of the Gymnasium.





- 4. Appears the contractor is in the process of cleaning the brick veneer.**



- 5. It appears the contractor has also cleaned the south wall of the gymnasium CMU and glazed CMU.**





6. Closer view of cleaned CMU. I stated my concern that it appears there is efflorescence that has not been cleaned off. The Architect stated it is differential drying not efflorescence.



7. Closer view of cleaned brick veneer. It appears there are locations that need further cleaning. Contractor needs to get the CMU and brick veneer cleaned, dried and sealed before weather turns.





8. Appears the contractor is setting the fence posts at fence on the south end of the building.



9. More fence posts being set south of the building and to the west.





10. More fence posts being set along Terre View Drive south and southwest of the building.

In the background you can see the sod being placed on the lower play field.



**11. Photo looking northeast:
Sod placement is underway.
Also note the landscaper is also watering the placed sod.**





- 12. Looking south, Kamiak is to the left. It appears the contractor has installed the sprinkler lines, no sprinkler heads on them yet.**



- 13. Same location as above photo looking north.**





- 14. It appears all the asphalt west of the building is placed.**



- 15. Contractor is taking delivery of more aluminum door frames.**





- 16. Contractor is placing sidewalk north of the gymnasium.**



- 17. It appears the developer has hydroseeded the borrow area.**





- 18. It appears the developer has hydroseeded the borrow area.**



- 19. Contractor is in the process of priming (block filler) the interior gymnasium walls.**





- 20. Contractor has cleaning crew on site, vacuuming dust off Commons floor.**



- 21. Contractor continues piping in Mechanical room.**





- 22. In Library: Circular lighting has been hung. Exposed ductwork and steel has been painted.**




- 23. Area A lower level: Corridor lighting is installed and powered up.**





- 24. Gang bathroom in Area 1 lower level has been tiled. Grout has not yet been placed.**

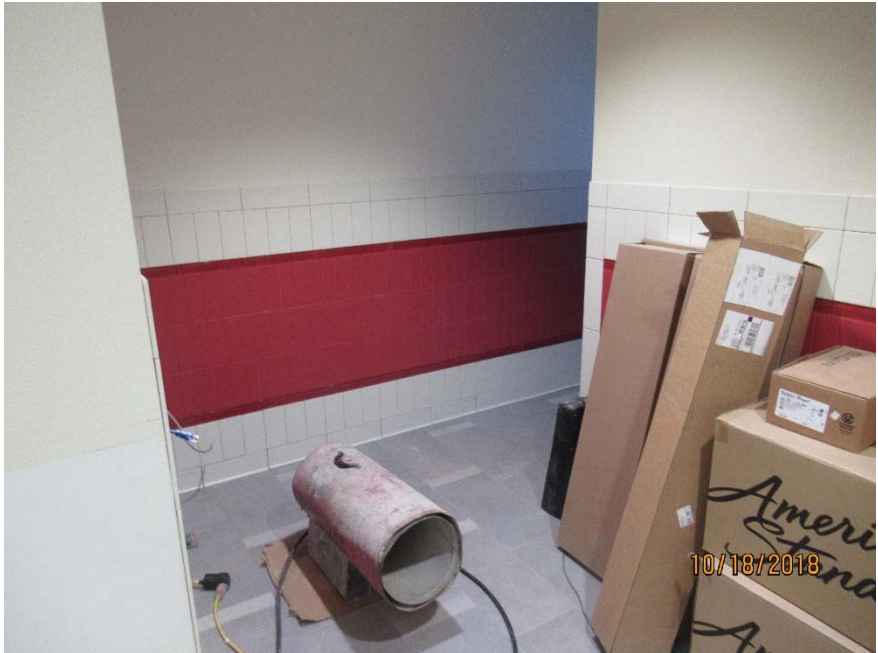

- 25. Area A upper level: Ceiling grid in corridor has been placed.**





**26. Casework installation in
Area A upper level is
underway.**



**27. Casework installation in
Area A upper level is
underway.**





28. It appears the contractor is nearly done finishing the wallboard in the main entry.



29. Contractor has taken delivery of Owner provided paper products. The toilet paper dispensers do not meet District quality control, so District will be returning and replacing them as soon as possible.



Deficiencies: Covering the HVAC diffusers an ongoing issue not yet addressed.

Dan Gordon
Project Manager

