








**Project: PSD: Kamiak Elementary School****Date: November 1, 2018****Weather conditions:**

Date	Hi/Low	Precip	Snow		Forecast	Avg. HI / LO
Thu 11/1	57°/49°	0.3 IN	0 IN		A brief shower or two	52°/34°
Fri 11/2	59°/41°	0.18 IN	0 IN		Mostly cloudy, a little rain	51°/34°
Sat 11/3	52°/42°	0.08 IN	0 IN		Times of clouds and sun	50°/33°
Sun 11/4	53°/37°	0.23 IN	0 IN		Periods of rain; breezy	50°/33°
Mon 11/5	48°/36°	0.1 IN	0 IN		Mostly cloudy, a few showers	49°/33°
Tue 11/6	47°/32°	0.05 IN	0 IN		Sun and clouds, a shower	49°/33°
Wed 11/7	46°/30°	0 IN	0 IN		A couple of showers possible	48°/33°

Discussion with: See Construction Progress Meeting dated 10/25/18.**Construction Activities:**

1. Temp road (less rock) still in place. Contractor expects this to be graded out by 11/9/18 or beginning of following week.





2. Contractor has formed for north sidewalk.



3. Contractor preparing north parking lot for asphalt.





4. Contractor has formed radiused curb. Will likely place concrete when they place sidewalk.



5. Contractor spreading and compacting north parking lot subbase gravel. The area between the arrows on this photo felt spongy. Contractor told me they are getting testing performed by GPI.





6. It appears the contractor has placed some of the topsoil north of the gymnasium.



7. The contractor appears to be forming for the stairs west of the entry by Library. There appears to be piles of top soil in what will be grass areas.





8. It appears the contractor has a portion of the play area between the 4 foot fence and the Asphalt fire lane top soiled and irrigation with heads. There is however still a large pile of soil in the middle.



9. It appears the area just west of the above mentioned also has irrigation and top soil placed.





10. Looking north at areas mentioned in photos 8 and 9.



11. The electric car charging station appears to be installed and energized. The “Power” light is illuminated





12. Contractor is painting the Gym and Multi-Purpose CMU walls.



13. It appears the contractor is installing wallboard ceiling around the installed projection screen.






- 14. Contractor has installed the Kitchen Type 1 canopy hood as well as the stainless steel wall protection.**



- 15. It appears rather than submitting a letter requesting the use of the building heating system, the contractor has elected to heat the gymnasium with temporary heating.**

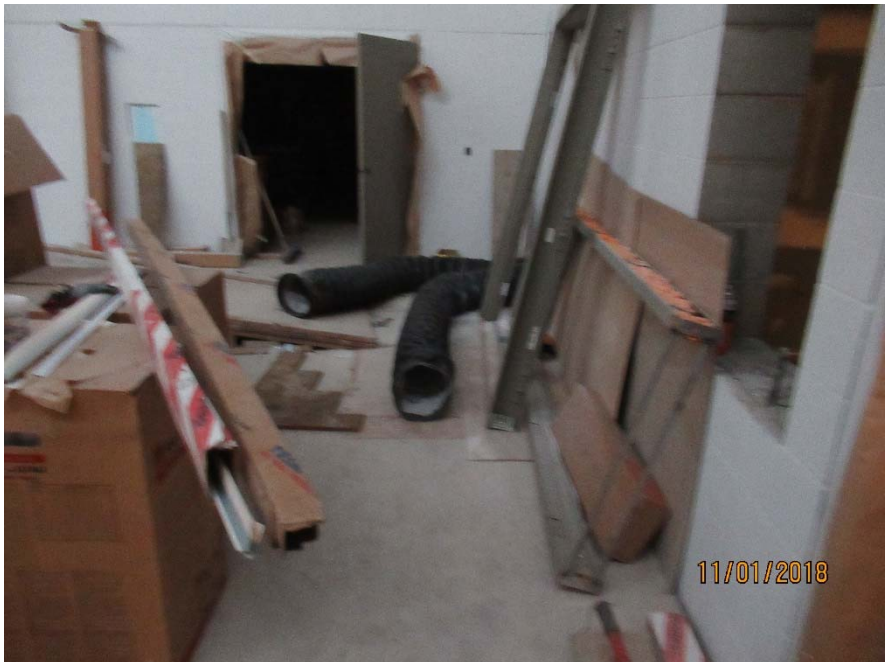



- 16. It appears the contractor has installed the gymnasium speakers. There is still now cover protection against dust into the duct work, and now no protection of speakers from dust.**



- 17. Upper level: casework has been staged in rooms. Some has been installed, much more to be installed.**





- 18. Upper level: casework has been staged in rooms.**



- 19. Upper level corridor it appears painting is nearly complete, wall in this picture appears to be prepared to receive tackable wall surface and reinforced panels.**





- 20. Upper level: casework has been staged in rooms.**



- 21. This appears to be the last toilet room to be tiled. Contractor installing floor today.**





- 22. Upper level: casework has been staged in rooms. Some has been installed, much more to be installed.**



- 23. This is a photo of the south end of the vinyl site obscuring fence. There appears to be an alignment issue to be addressed. As the overall fencing is not yet completed it is likely something the contractor is still working on and this is not the finished product.**





24. It appears the curb installation was not aligned with the driveway entrance apron or the pavement. Architect will address this with contractor.



25. It appears the curb installation was not aligned with the driveway entrance apron or the pavement. Architect will address this with contractor.



Deficiencies: Covering the HVAC diffusers an ongoing issue not yet addressed. The architect will address the curb miss alignment with contractor.

Dan Gordon
Project Manager

