








**Project: PSD: Kamiak Elementary School****Date: November 15, 2018****Weather conditions:**

Date	Hi/Low	Precip	Snow	Forecast	Avg. HI / LO
Thu 11/15	51°/38°	0.06 IN	0 IN	 Mostly cloudy	44°/31°
Fri 11/16	48°/29°	0 IN	0 IN	 Mostly cloudy	44°/31°
Sat 11/17	43°/26°	0 IN	0 IN	 Sunny	43°/31°
Sun 11/18	43°/28°	0 IN	0 IN	 Mostly sunny	43°/30°
Mon 11/19	43°/27°	0 IN	0 IN	 Sunshine	42°/30°
Tue 11/20	45°/28°	0.06 IN	0 IN	 Mostly sunny	42°/30°
Wed 11/21	43°/31°	0 IN	0 IN	 Considerable cloudiness	41°/30°

Discussion with: No Construction Progress Meeting today 11/15/18. I toured the project with Ned Warnick, Derek Oliver, Joe Thornton and Evan Hecker.

Construction Activities:

1. Contractor appears to be finishing laying asphalt at a portion of the North parking lot that they didn't get done yesterday. As you will see in photo 8 below, the asphalt contractor moved to the south play area while I toured the building.





2. **Appears the contractor is striping North parking lot that was asphalted yesterday.**



3. **The contractor has not fixed the vinyl fence nor have they picked up the fence pieces strung across the play field.**





4. It appears the landscaper is done for the year. There has been no change to the south play area.



5. The contractor has placed some of the lighting in the gymnasium.





6. It appears the painter is painting the ductwork in the Multi-purpose room.



7. Contractor has installed some of the lighting in the upper level corridors.





8. The asphalt contractor appears to be setting up to [place asphalt at the hard surface play area at the south playground.



9. It appears the contractor has roughed in the pond north of the north parking lot.






- 10. It appears the contractor is installing glazing in the interior classroom windows. The glass is loose in the frame. See below.**



- 11. It appears the contractor is installing 1/4" tempered glass. This is incorrect because this was changed to laminated safety glass (two layers of 3/16" thick clear float glass, laminated with 0.060" thick poly vinyl butyl interlayer) with the acceptance of PR-25 on 8/23/18.**

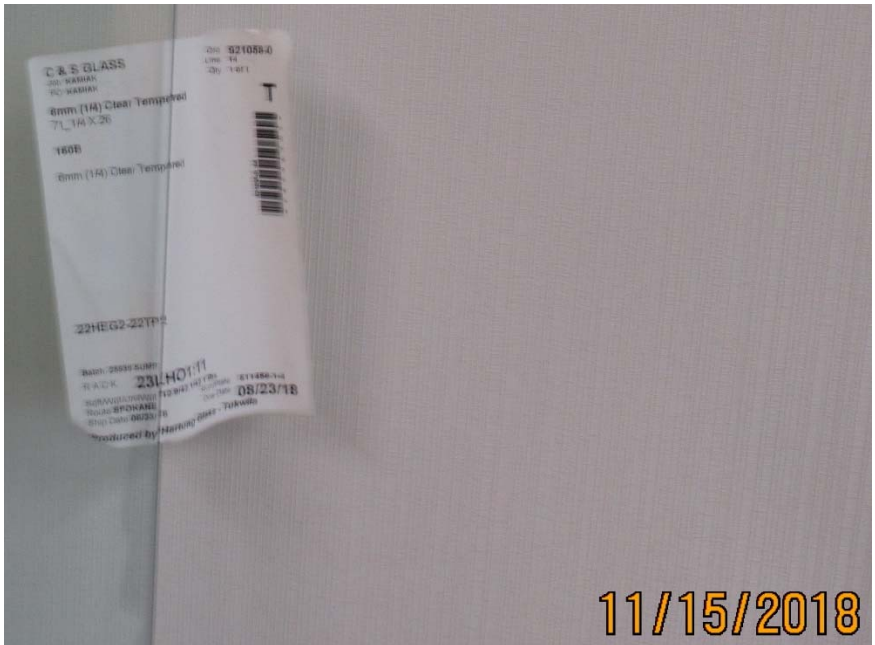

Deficiencies: Covering the HVAC diffusers an ongoing issue not yet addressed. The tall storefront at breakout spaces has not yet been sealed on the inside between floors. Both these issues are addressed in the commissioning issues log. Contractor installing incorrect glazing in interior window frames.

Dan Gordon
Project Manager

