










Observation Report

Dan Gordon, Senior Project Manager
P: 509.323.2748 - F: 509.323.2758

Project: PSD: Kamiak Elementary School

Date: February 15, 2018

Weather conditions:

Date	Hi/Lo	Precip	Snow	Forecast	Avg. HI / LO
Thu 2/15	32°/26°	0.04 IN	0.4 IN	 Partly sunny	41°/27°
Fri 2/16	40°/34°	0.45 IN	0.3 IN	 A bit of snow and rain	41°/27°
Sat 2/17	43°/30°	0.24 IN	0 IN	 Breezy with periods of rain	42°/27°
Sun 2/18	34°/14°	0.06 IN	0.6 IN	 Cloudy with a little snow	42°/27°
Mon 2/19	22°/7°	0 IN	0 IN	 Mostly cloudy	42°/27°
Tue 2/20	25°/12°	0 IN	0.1 IN	 Sunshine, but very cold	42°/27°
Wed 2/21	34°/20°	0.14 IN	2.3 IN	 Considerable cloudiness	42°/28°

Discussion with: See Construction Progress Meeting dated 2/15/18.

Construction Activities:

1. Appears the contractor has set the chiller on its pad.





2. Contractor has accepted delivery of HRU-1. This unit will be set near the north end of the Mezzanine.



3. Contractor has accepted delivery of HRU-2. This unit will be set near the South end of the Mezzanine.





4. Appears masons continue laying up CMU along gridline T.



5. Steel structure erection in Area B continues. Note that the northern stair has been placed.





6. Steel structure erection in Area B continues. Note that the Main Entry stair has been placed.



7. Photo looking south along the east exterior wall.





8. . Photo looking south along the west exterior wall.




9. Appears the contractor has placed the welded wire fabric on the second floor. Still needs to be put on highchairs to center it in the slab when poured.





10. Appears framing of the east wall of the mezzanine continues. Also although difficult to see in this photo the cement board floor is installed from where the workers are to the north to grid line M.

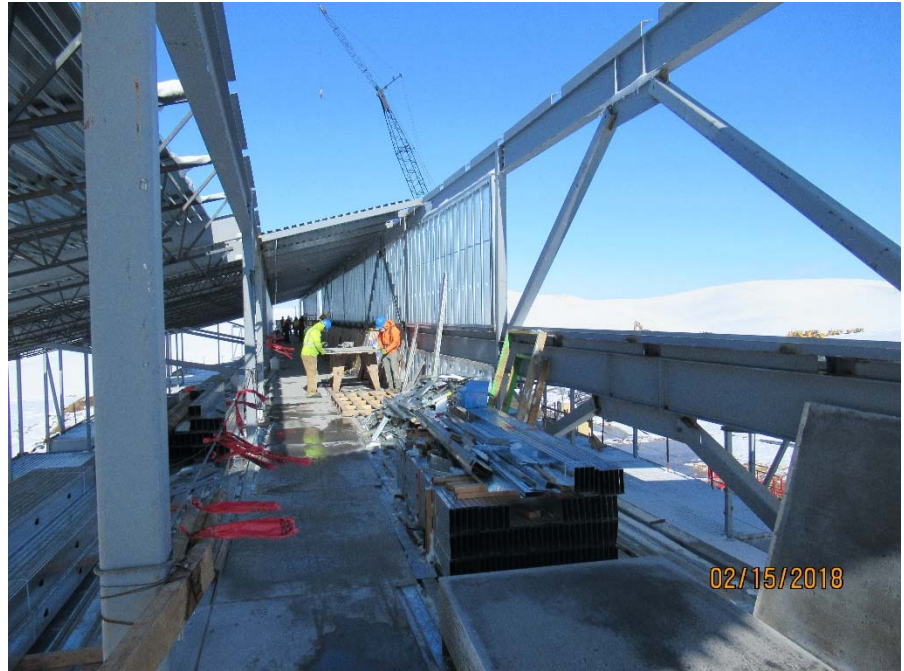

11. Appears that Mader/DebCo has lined the lower pond east of TerreView and is pumping the area out to south of District property. It also appears the contractor has poured die on the ice.



Deficiencies: None noticed at this time.

Dan Gordon
Senior Project Manager

