





## Observation Report

Dan Gordon, Senior Project Manager  
P: 509.323.2748 - F: 509.323.2758

**Project: PSD: Kamiak Elementary School**

**Date: February 8, 2018**

### Weather conditions:

Date	Hi/Lo	Precip	Snow	Forecast	Avg. HI / LO
Thu 2/8	56°/31°	0.09 IN	0 IN	 Clouds and sun with a shower	40°/27°
Fri 2/9	41°/22°	0 IN	0 IN	 Mostly cloudy and cooler	40°/27°
Sat 2/10	38°/25°	0 IN	0 IN	 Mostly sunny	40°/27°
Sun 2/11	44°/30°	0.04 IN	0 IN	 Rain and drizzle in the p.m.	40°/27°
Mon 2/12	42°/27°	0.02 IN	0 IN	 Variably cloudy with a flurry	40°/27°
Tue 2/13	43°/33°	0 IN	0 IN	 Partly sunny	41°/27°
Wed 2/14	49°/36°	0.01 IN	0 IN	 Rain and drizzle possible	41°/27°

**Discussion with:** No Construction Progress Meeting today. Met with DOE concerning storm water control.

### Construction Activities:

1. Masons continue laying up CMU at Gymnasium, Kitchen and Stage.





**2. Masons have begun laying CMU on the north, south and east walls of the Gymnasium.**



**3. Masons have begun laying CMU on the south wall of the Gymnasium and it appears they are close to topping off the connection points for steel structure.**







**4. Appears the contractor has taken another delivery of structural steel. Photo shows another stairway.**



**5. Appears the contractor has taken another delivery of structural steel.**





**6. Contractor has placed the lower floor slab on grade from grid line A to M.**



**7. Wall framers continue framing exterior walls. Appears east exterior walls are framed from grid line A to M.**








**8. It appears the contractor has installed the second floor metal decking and anchor studs.**



**9. Appears the contractor has placed roof decking on the western half of roof over area between Grid lines A to M. Also appears the framing of the lower portion of the east wall of the mezzanine is underway.**

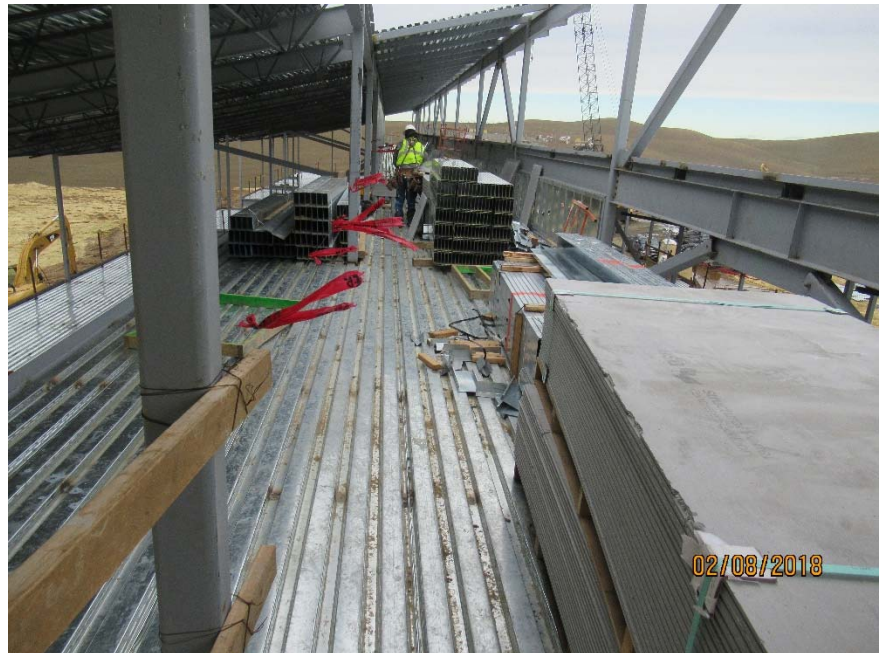

**Deficiencies:** None noticed at this time.

**Dan Gordon**  
Senior Project Manager

