








**Project: PSD: Kamiak Elementary School****Date: January 10, 2019****Weather conditions:**

Date	Hi/Low	Precip	Snow	Forecast	Avg. HI / LO
Thu 1/10	48°/32°	0 IN	0 IN	 Mainly cloudy	36°/25°
Fri 1/11	42°/30°	0 IN	0 IN	 Sunshine and some clouds	36°/25°
Sat 1/12	42°/27°	0 IN	0 IN	 Mostly sunny	36°/26°
Sun 1/13	40°/28°	0 IN	0 IN	 Partly sunny	36°/26°
Mon 1/14	39°/29°	0 IN	0 IN	 Partly sunny	37°/26°
Tue 1/15	40°/33°	0.01 IN	0 IN	 Clouds and sunshine	37°/26°
Wed 1/16	41°/34°	0.06 IN	0 IN	 A couple of flurries possible	37°/26°


Discussion with: See Construction Progress Meeting minutes dated 1/10/19**Construction Activities:**

1. Contractor has finished gymnasium floor, currently installing vented wall base. There is some issue with thresholds the Architect is working through with the Contractor.






2. This is a better photo of the holes drilled in the outside of the box for the projector that will be in the soffit between the gym and multi-purpose rooms.

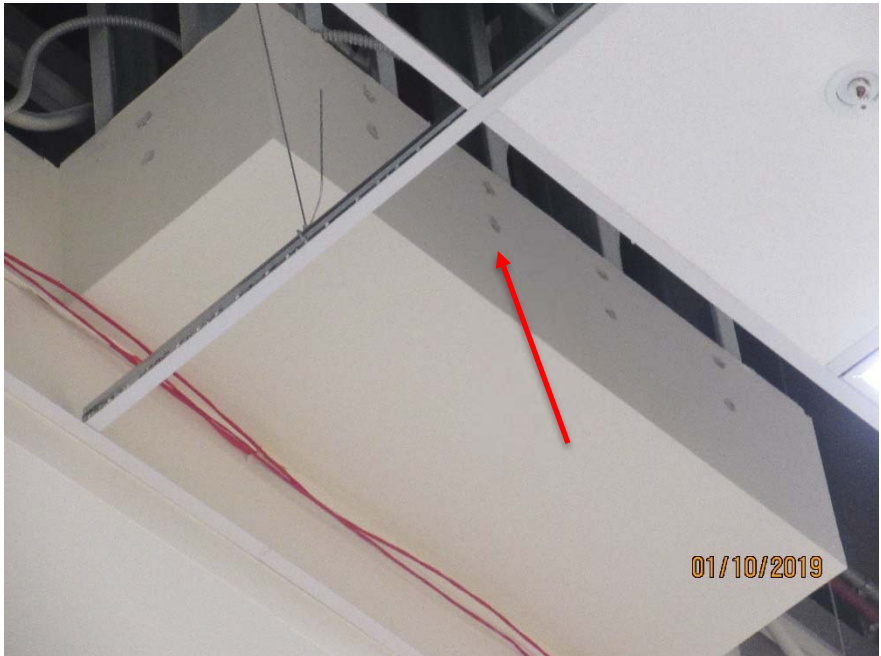

3. This is a photo of the holes drilled in the inside of the box for the projector that will be in the soffit between the gym and multi-purpose rooms.

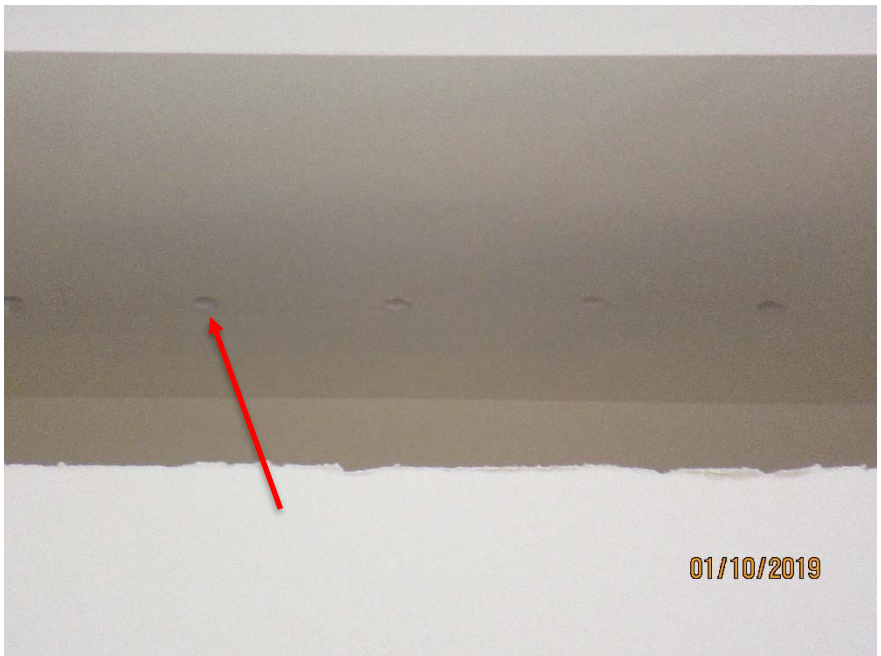



- 4. Casework installer continues installing casework throughout the building. This photo is on the stage.**



- 5. Appears the contractor has installed strip lighting in soffit at stage.**





6. Contractor has adjusted fire sprinkler heads and finished installation of drop in ceiling in Library.



7. It appears the contractor has taken delivery of the correct, laminated glass for the interior windows.






- 8. Installation of Admin work stations appears to be underway.**



- 9. Contractor has begun installing glass in door relites.**

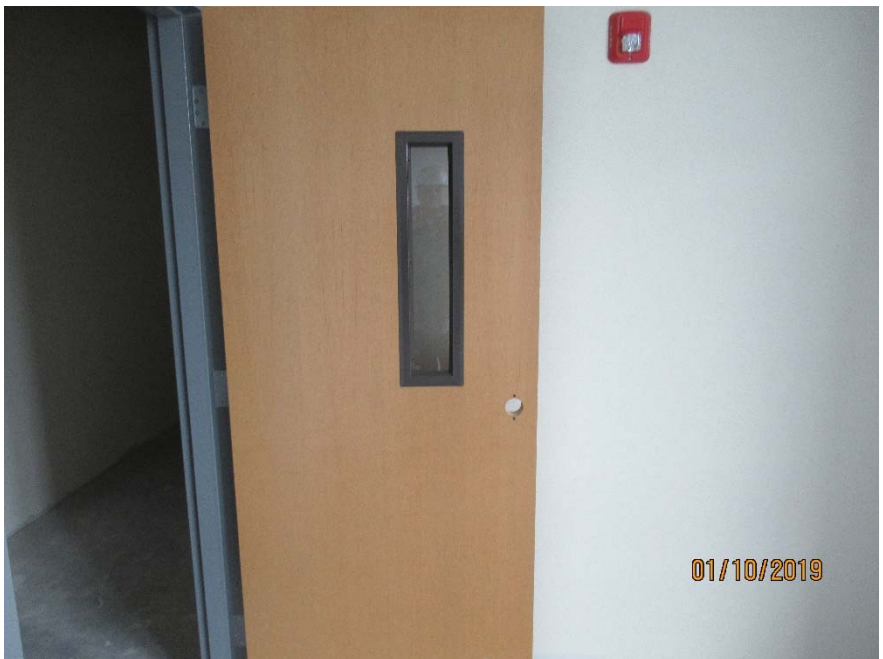



10. It appears to me that the blue on the right in this photo is incorrect. This is the only place in the building that has this shade of blue. I believe it should be like the blue on the left side of this photo. I have notified the Architect.



11. Appears the contractor has cleaned up and painted the stair stringers.





12. This photo is of the hand wash station outside Restroom 114. I notified the contractor that the column and cap are out of plumb.



13. Contractor appears to be prepping the expansion joint in the corridor for floor finish.






- 14. Contractor has installed the upper floor wood ceiling. Note the contractor has removed the p-trap that was projecting into the soffit space. Wallboard will be repaired.**



- 15. Contractor has replaced clear glazing in Storage Room 243 with spandrel glass per submittal.**

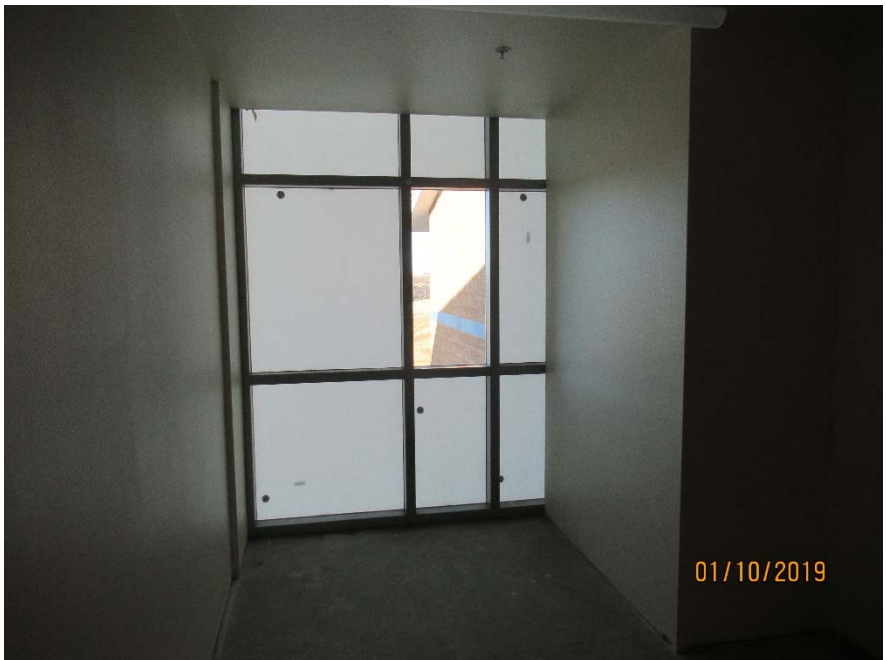



- 16. Contractor has finished removal of the cover at the monument sign and flag pole.**



- 17. I notified the contractor that it appears the exterior brick wall above and north of the Library does not appear to have been cleaned. This will need to be cleaned as well as any other spot locations before the sealer is applied.**



Deficiencies: No deficiencies noticed at this time.

Dan Gordon
Project Manager

